MULTI-NATIONAL FORCE - IRAQ Progress Update

القوة متعددة الجنسيات - العراق

تحديث للتقدم



الاميرال غريغ سمث و العميد جيفري دوركو والدكتور تحسين الشيخلى

2008 February 3 2008 شباط 3 www.MNF-Iraq.com



Health and Education Partnerships



Health Partnership

	Investment	# Projects
New Primary Healthcare Clinics	\$254M	142
Hospitals	\$288.5M	25
Health Clinic Repairs	\$31.4M	285
Total	\$573.9M	452

- 142 new Public Healthcare Clinics 76 completed
- 25 renovation projects at 20 hospitals 17 completed
- Construction on 2 new hospitals Maysan and Basrah Province

Primary Healthcare Centers

Iraqi Relief and Reconstruction Fund

Program Cost: \$254M

Scope of Work: Construct 142 PHCs throughout Iraq


Status of Work

• Program percent complete: 95%

• Estimated completion PHC Program: May 08

• PHC status

- **76** PHCs turned over to the Ministry
- **20** in post construction phase
- **35** under construction
- **4** delayed for security or contractor issues
- **5** were destroyed and have been cancelled
- 2 were destroyed and have been reprogrammed

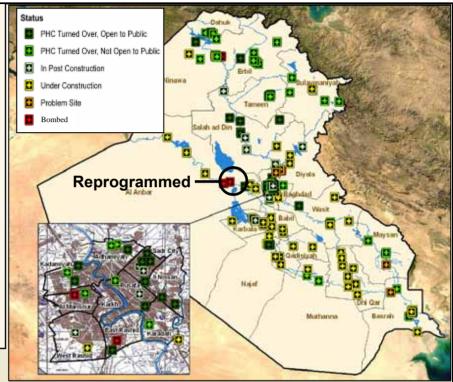







Primary Healthcare Centers

In Post Construction Under Construction

Problem Site


Bombed

Baghdad Area


- Of 30 planned PHCs, 21 are completed and turned over to the Ministry
 - 13 PHCs open to the public
 - 8 PHCs turned over to Ministry-not open to public

•PHC status

- 5 PHCs in post-construction phase
- 2 PHC had work stoppage due to lack of security
- 2 De-programmed sites (bombed)

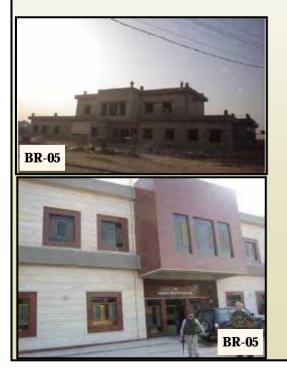



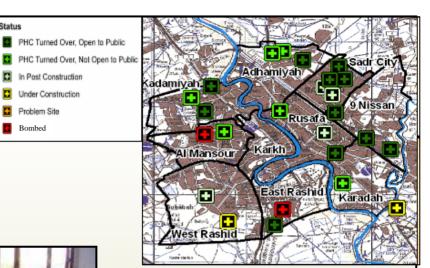





Primary Healthcare Centers

Location: Baghdad Province

Completed: 15 Mar 06 **Opened:** 24 May 06
















Hospitals

Ibn Al Baladi Hospital **Location**: Baghdad **Completed**: 29 Dec 07













OPERATING ROOM









Basrah Children's Hospital

Program: World class clinical and training facility for pediatric specialty care with a focus on oncology

Project Cost: \$163.1M

Scope of Work

- Modern 2-story, 94-bed clinical & training pediatric oncology hospital, 2 utility buildings, 36-bed residence hall
- Medical equipment procurement, installation, and commission
- Train admin, facility engineers, and biomed engineers
- Medicine, service contracts, linens, uniforms, vehicles


Status of Work

• Program percent complete: 70%

• Estimated completion: Jul 08

• Employment: Average **700** workers/day on the jobsite



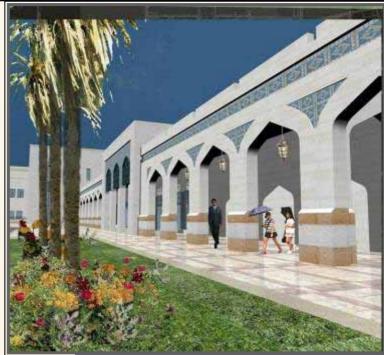



Education Partnership





	Investment	Number
New Work	\$259.1M	1,885
Repaired Schools	\$ 95.5M	1,604
School Equipment/Supplies	\$ 18.6M	
TOTAL	\$373.2M	3,489






Southern Region Mud School Before & After



Al Fursan School for Girls Teachers Training Institute

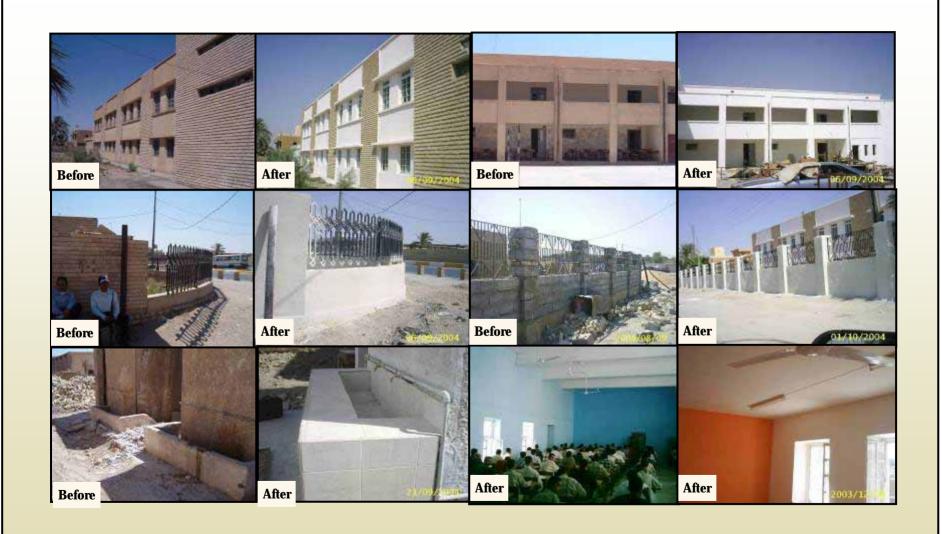

Health and Education Partnerships



MULTI-NATIONAL FORCE - IRAQ Progress Update

القوة متعددة الجنسيات - العراق

تحديث للتقدم



الاميرال غريغ سمث و العميد جيفري دوركو والدكتور تحسين الشيخلي

2008 February 3 3 شباط 2008 www.MNF-Iraq.com

